Tokmanni Group Oyj

Modernise legacy tools and reporting without disturbing store operations, with margin data locked to the right roles

Draft staffing revision - candidate evidence, scope and rates require owner confirmation

A 22-week delivery plan with explicit staffing capacity and price

- **Outcome measured in your ledger, not in hypothetical hours:** named legacy tools and reports switched off, and their running costs removed (target list agreed in month 1)
- **Margin data protected by design:** row- and role-level security on by default; margin figures visible only to roles your business owners approve; access tested before every go-live
- **Stable daily operations:** releases outside store peak hours and campaign weeks, parallel running, tested rollback per app
- **Team that works your way:** Finnish-speaking, on site in Mäntsälä 2 days per week, follows your central office routines
- **Builds on what you have:** your BI tool, public cloud and ERP programme; no new licences; the target stack is confirmed with you in phase 1
- **Draft EUR 218,625 capacity fee** across three gates; confirm scope and risk allowance before a binding fixed-price commitment.

Margin figures stay with the people entitled to them: access is closed by default and tested

- **Deny by default:** a new report or app shows nothing until a role grants it. Margin and purchase-price columns are classed as sensitive and hidden unless the role allows them.
- Access rules live in code, and an automated test runs on every release: "store supervisor cannot see department margin" fails the release if broken.

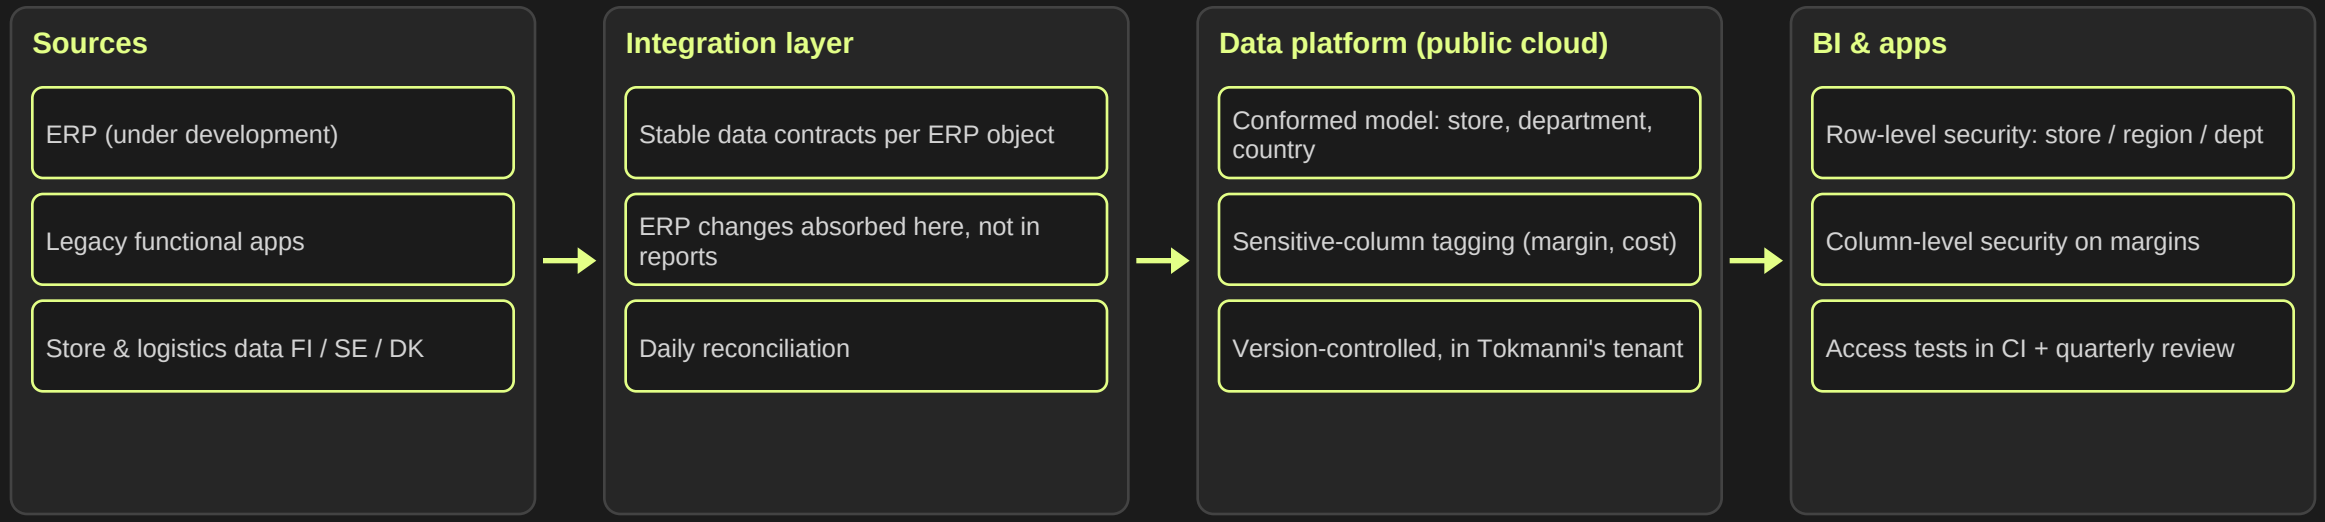

Access maps to your BI tool's native roles; without column-level security, margins are masked in the data layer · apps replaced one at a time, tested rollback

Deliverables: D1 inventory (keep / migrate / retire) · D2 role matrix signed by business, security tests in CI · D3 governed data layer, ERP interfaces via data contracts · D4 priority reports FI/SE/DK · D5 functional apps only where they remove cost · D6 Finnish runbooks and training.

Three gated phases fit around retail seasons

Phase	Timing	Content	Gate
1. Discovery & access model	6 planning weeks	Inventory, role matrix, ledger-cost baseline per tool, data-access probe on 3 priority tools, go/no-go risk report	You approve the list and access model
2. Build wave 1	8 planning weeks	Data layer, priority reports, access tests, parallel run	Supervisor pilot in agreed stores; access tests pass; retirement targets set against each tool's baseline
3. Build wave 2 & retire	8 planning weeks	Functional apps, remaining reports, switch-off, handover	Legacy tools switched off, ledger lines removed

No go-lives during Christmas season or major campaign weeks; freeze calendar agreed with store operations in phase 1.

Proposed role mix, allocations and verification before commitment

- Replacement at your request: equal seniority within 10 working days, 2-week overlap at our cost
- You may recruit our consultants after 12 months, with no fee
- Written update every second week and a monthly steering; decisions logged, no extra status meetings

Proposed role	Role	Allocation	Required certificates
Engagement lead	Engagement lead, Mäntsälä on site	40%	Microsoft Certified: Azure Data Engineer Associate
Lead data engineer	Lead data engineer	100%	Databricks Data Engineer Professional, Azure Data Engineer Associate
BI & security developer (Swedish too)	BI & security developer (Swedish too)	80%	Microsoft PL-300 Power BI Data Analyst, SC-900

Draft role profiles: nominate consultants and verify CVs, certificates, languages, dates and actual availability before submission. No person is booked by this draft.

EUR 218,625 for the stated 22-week capacity plan

- 7.5 h/day; 5 planning days/week. Lead 40%, DE 100%, BI/security 80%; 2.2 FTE, not two full-time people.
- DE EUR 115/h; BI/analytics EUR 125/h; proposed engagement lead EUR 125/h (owner confirmation pending).
- Confirm exact dates, holiday calendar, access and scoped deliverables at the discovery gate; releases remain outside peak and campaign windows.

Phase	Draft fee	Role-days (lead / DE / BI)
1 Discovery: 6 weeks	EUR 59,625	12 / 30 / 24 = 66
2 Build: 8 weeks	EUR 79,500	16 / 40 / 32 = 88
3 Handover: 8 weeks	EUR 79,500	16 / 40 / 32 = 88
Total, excl. VAT	EUR 218,625	44 / 110 / 88 = 242

Candidate evidence and availability pending. Existing licence claims require client confirmation; consumption and travel excluded. Final fixed-price scope and risk allowance require owner review.

Staffing review and decision before submission

- Rauno / Codex staffing review: maximum two architects respected; complementary roles included; DE/DA floors and AI premium applied to the stated role scope.
- This revision replaces the lower draft price for the same capacity. If the buyer budget is lower, reduce scoped work or hours and re-estimate; do not discount below hourly minima.
- Candidate CVs, credentials, language skills, exact dates and actual availability remain unverified. Nominate and confirm before buyer submission.
- Final fixed-price deliverables, risk allowance and the proposed non-DE rates require offer-owner review. This is not a human approval or a request to send.
