RECORDLY

Analytics tickets in, reviewed pull requests out

An agent that drafts the code. Your people approve every change. Everything stays in Aktia's perimeter. €61,080 fixed total, Aktia's standard terms.

Proposal to Camilla Engblom, Head of Data and Analytics · Recordly Oy · Helsinki

Supplier profile, financial standing, subcontractors

Supplier	Recordly Oy, Helsinki. Data and AI consultancy. Our own agent product, the Virtual Data Engineer, is the pattern we propose here
Financial standing	Latest financial statements and a third-party credit report supplied with the formal tender
Subcontractors	**None.** Recordly employees only. Any later change needs Aktia's written approval


Concrete AI implementation case examples

CASE (RECORDLY AGENT TEAM ON SNOWFLAKE + DBT)	MEASURED RESULT
Semi-complex pipeline: build, test, validate. A person approves the PR	**12 h by hand → 30 min**
Migration Matillion + Redshift → dbt + Snowflake, jobs included	**~30 Snowflake credits** per migrated table
Pipeline and availability questions answered in the chat thread	Developer context switches per day: **several → 0**

> These are our results, not Aktia's. Your own baseline (ticket lead time, review load) is measured in Definition, so the pilot is judged on your numbers.

Technical solution architecture

One loop, inside Aktia's cloud tenant. The agent never merges.

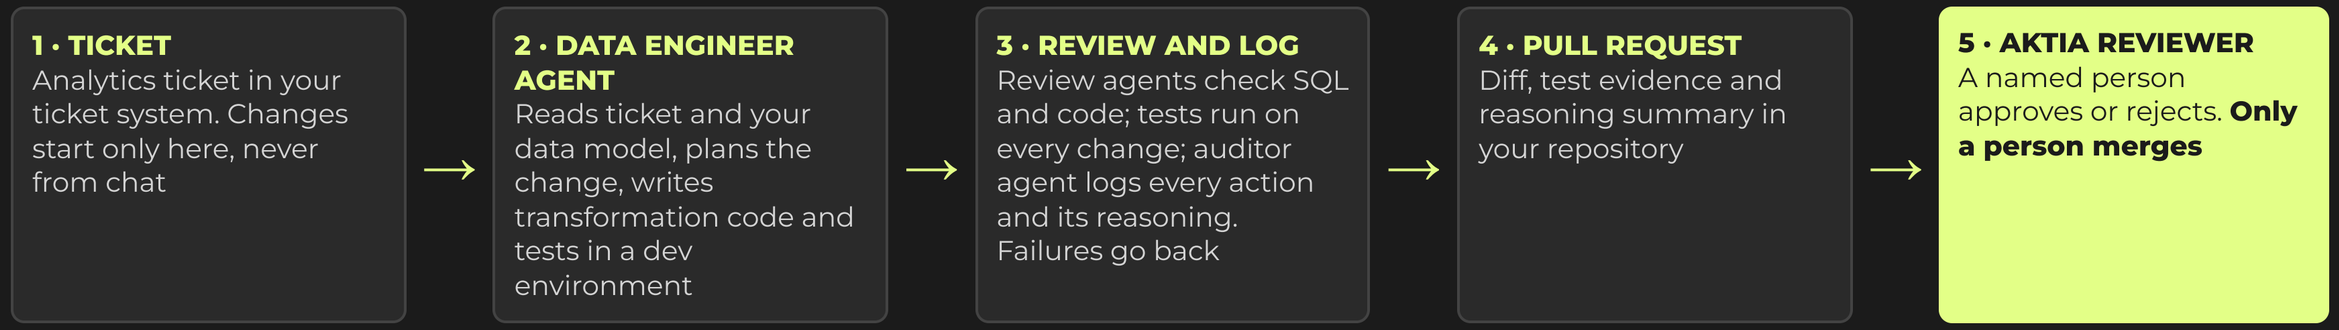

PERMISSIONS: the agent writes only to its own branches and a dev schema, holds no production credentials and cannot push to protected branches. Code, data, logs and model calls stay in Aktia's tenant; audit log retention follows your policy. Temenos Transact is read for reporting data only; no core changes.

- **Your stack, honestly:** the RFP says "current data setup" and "public cloud". Our proven pattern runs in Snowflake with dbt. Your ticket system and git platform are assumed, not known. **Definition week 1 confirms all three.** If it is not Snowflake + dbt, we adapt the same guardrails to your stack and re-agree scope at the gate. You can stop there.
- **Out of scope:** ML models or anomaly detection, new BI tools, extra use cases, any change to Temenos Transact. Only ticket → code → tests → pull request.

Compliance posture: FIN-FSA, EBA, DORA

WHAT YOU TOLD US	WHAT WE BUILD IN
Last winter a script bypassed peer review and altered schema dependencies	The agent **cannot approve or merge its own work.** Branch protection needs a named Aktia reviewer. Changes touching schema dependencies are blocked until the data owner approves
Supervisors scrutinise foreign-headquartered AI API dependencies	Definition delivers model-hosting options: models served in your own tenant in an EU region, no ticket text, code or data to external APIs, every provider named with an exit plan
AI governance and operational resilience	Auditor agent keeps the audit trail. A bad merge is reverted by a normal revert PR and logged in your DORA incident process. The agent stops when stuck. A control matrix maps each control to FIN-FSA, EBA and DORA requirements. Aktia compliance signs it off; we do not certify
Runbooks in English caused friction	Matrix, runbooks and training in **Finnish and Swedish**
IP	Everything made for Aktia (code, prompts, conventions, docs) is Aktia's property, stated in the contract

Unknown we will test: whether an EU-hosted model is good enough, run on 20 of your tickets at the Definition gate. If it falls short, scope narrows to simple ticket types. No external API fallback.

Core team: three seniors who do the work

	LEAD DATA ARCHITECT	SENIOR DATA ENGINEER	SENIOR AI ENGINEER
Required certifications	SnowPro Advanced: Architect · dbt Analytics Engineering	SnowPro Core · dbt Analytics Engineering	SnowPro Core · Microsoft Certified: Azure AI Engineer Associate
Required languages	Finnish required, Swedish, English	Finnish required, English	Finnish required, English
Availability	From signature, start date fixed in the contract	From signature	From signature

- **Swedish:** every Swedish deliverable is reviewed by a native Swedish speaker before delivery
- **Key-person terms:** named people, substitution only with Aktia's approval, equal seniority, overlap at our cost, financial penalty if breached. Aktia may require replacement at any time

Delivery plan and timeline

PHASE	WEEKS	WHAT HAPPENS	GATE
Definition	1–3	Confirm stack. Baseline on 20–30 recent tickets. Control matrix (FI/SV). Model-hosting options. Pick 2–3 ticket types	**Aktia decides go/no-go**
Delivery	4–9	Conventions and "perfect examples" written with your engineers. Agent team deployed in your tenant. Supervised pilot on the chosen ticket types	Merged-without-rework rate, test pass rate, review minutes per PR, run cost per ticket vs baseline. Targets set at week-3 gate; a miss means stop or adjust
Ongoing operations	10–22	Agent in run mode on a fixed 3-month term. **Aktia staff approve every change.** About 1 architect day per month from us	Scale, adjust or stop

- Your engineers co-build from week 1 and own conventions, prompts and code. Nothing is handed over at the end
- **No status meetings.** Written update every two weeks
- **Unknowns:** ticket quality (unclear tickets get questions back, not guesses; measured on the baseline set) and stack fit (week 1)

Preliminary pricing: definition, delivery, ongoing operations

Fixed total: €61,080 (excl. VAT)

PHASE	DAYS × DAY RATE	AMOUNT
Definition	AI architect 5 d × €960 + AI engineer 3 d × €960	€7,680
Delivery	AI architect 8 d × €960 + Data engineer 12 d × €920 + AI engineer 5 d × €960	€23,520
Ongoing operations	Agent team 3 months × €9,000 + AI architect 3 d × €960	€29,880

- **36 human days at €920–960/day**, plus the agent team on a **fixed 3-month term from go-live**. Pilot runs in Delivery are included
- **Stop after Definition** and pay only that phase. Invoiced per phase on acceptance, 21 days net
- **Licences:** none from Recordly. If you run Snowflake, AI credits are consumed on your account and billed by Snowflake
- **No contractual deviations.** Aktia's standard terms and key-person penalties accepted

Staffing review / Rauno: role profiles are requirements, not verified people. Confirm CVs, certificates, languages and actual availability before submission. One day = 8 hours; DE minimum EUR 115/h, DA EUR 125/h, AI expertise adds EUR 5/h for the relevant specialist. Architect base EUR 115/h is proposed for owner confirmation, not a user-supplied minimum. At most two architects. Validate fixed scope and risk allowance before commitment.

Architect effort: definition 5 days + setup 8 + run review 3 = 16 days, including the AI premium. DE 12 + AI engineer 8 = 36 human days total. Customer approves run changes.
