Oriola Oyj

Data warehouse migration to Azure, proven on your own supply chain tables first

Recordly proposal | Pharmaceutical wholesale and distribution, Espoo

We migrate your DW to Azure in 9 months for €168,000, and prove velocity in 8 weeks first

- **Phase 1 (8 weeks, €38,000 fixed):** migrate real supply chain tables (orders, stock, deliveries) end to end and publish measured velocity: tables per week, defects, reconciliation rate
- **Then decide:** phases 2-3 go ahead only if the measured velocity holds; no multi-year lock-in
- **One standard, no one-off scripts:** a metadata-driven ingestion framework for every SAP S/4HANA and wholesale interface, same pattern in every warehouse environment
- **Reliable reporting:** reconciled Gold layer feeding your BI tool, with automated data tests
- **Team:** 3 of 4 named consultants to be confirmed in writing at signature; replacement on request accepted
- **Total €168,000** (phase 1 €38k + phase 2 €86k + phase 3 €44k)

One metadata-driven pipeline pattern replaces hand-crafted wholesale scripts

- Adding a wholesale or warehouse interface = **one config row + tests**, not a new script. The same template runs in every warehouse environment.
- Built only in Oriola's Azure tenant and Git; no new licences. Azure consumption estimated €2,500–4,000/month, confirmed from the pilot's measured loads.

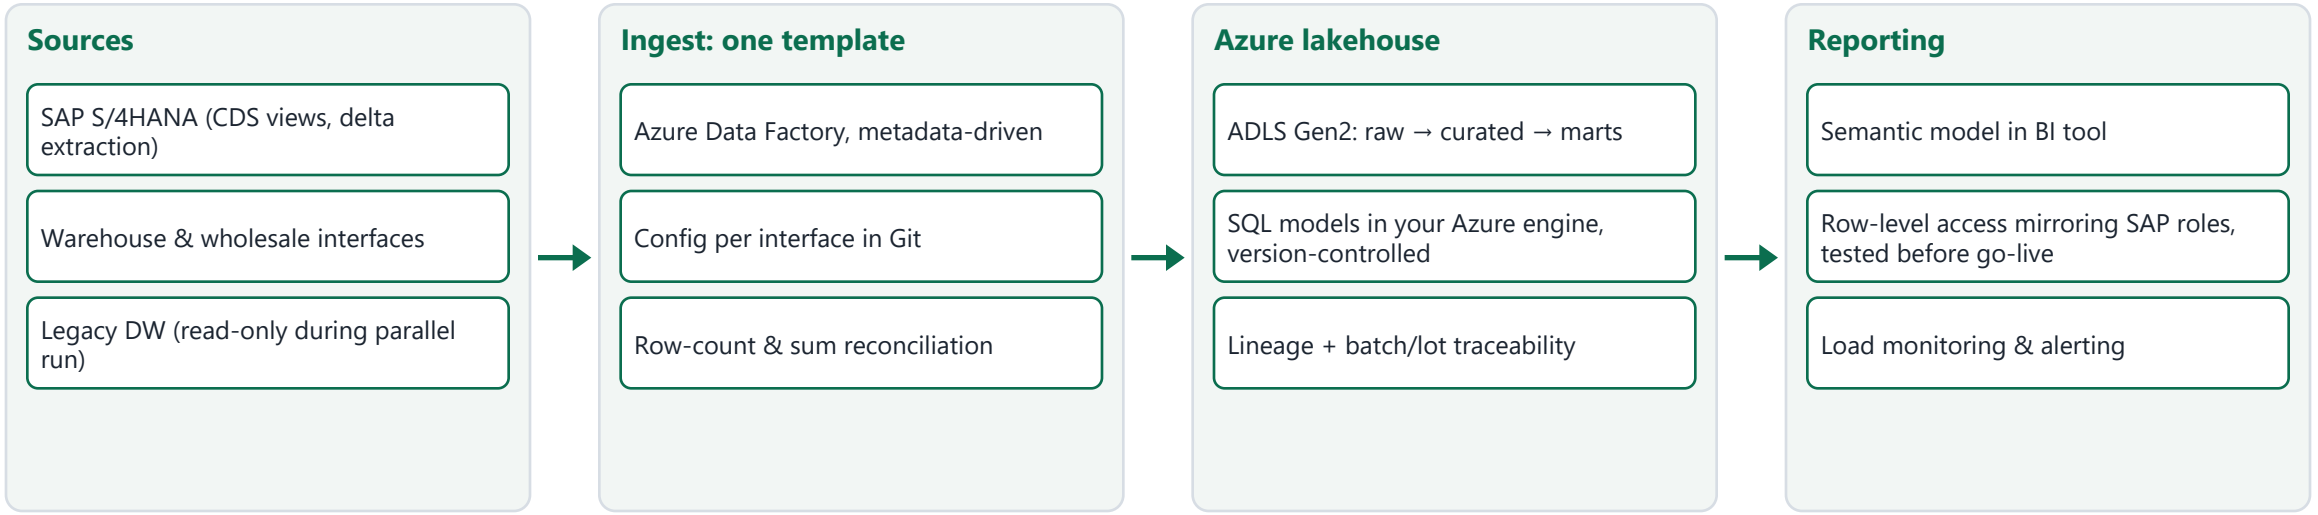

Parallel run: legacy stays read-only until reconciled totals match on consecutive loads; rollback = repoint BI to legacy · alerts with runbooks so incidents get fixed once

Week 1: probe SAP, interfaces and the legacy DW, inventory undocumented logic and confirm the ≤250-table assumption. Ingestion engine per interface type (Data Factory or alternative) chosen on measured throughput.

Three gated phases with measured velocity, not a big-bang programme

Phase	Months	Deliverables	Gate / metric
1 Velocity pilot	1-2	Framework v1, 15-20 supply chain tables migrated + reconciled, velocity report	Tables/week; targets confirmed after 2 weeks of measurement on 15-20 orders, stock and delivery tables (proposed: reconciliation ≥ 99.9%, ≥ 80% of interfaces config-only), no unrecovered load failure > 4 h: go/no-go
2 Core migration	3-7	All wholesale + warehouse domains on the framework, BI repointed	Monthly velocity report vs. plan
3 Cut-over + handover	8-9	Parallel run, legacy switch-off, runbooks, training	Business sign-off; your team operates

A proposed team, 3 of 4 confirmed in writing at signature, working side by side with your engineers

- **Reference 1:** Finnish wholesale distributor, SAP ECC → Azure lakehouse, 300 tables in 7 months
- **Reference 2:** Nordic healthcare logistics company, legacy SQL Server DW → Azure Databricks with automated reconciliation
- **Replacement:** you may request any consultant's replacement; equal seniority within 10 working days, 2-week overlap at our cost
- Pairing with your engineers from phase 1; workshops, runbooks and documentation in Finnish
- Written update every second week and a monthly steering; decisions logged, no extra status meetings
- You may recruit our consultants after 12 months, with no fee

Name	Role	Allocation	Certifications	Available
Antti Koskinen	Lead architect	60%	Azure Solutions Architect Expert, Databricks DE Professional	At signature
Mikko Laine	SAP data engineer	100%	SAP Certified Associate, Databricks DE Professional	At signature
Riikka Salo	Data engineer	100%	Azure Data Engineer Associate	At signature
Ville Nieminen	BI / test engineer	50% from month 3	Power BI Data Analyst Associate	Month 3

€168,000 total, paid per accepted milestone, with clear assumptions

- **Licensing:** no Recordly or third-party licences; Azure and BI licences billed to Oriola directly
- **Contract:** your standard terms accepted; you may stop after any gate and pay only accepted phases
- **Risks / assumptions:** up to 250 source tables; undocumented legacy logic is the main risk, measured in phase 1 and re-priced at the gate if needed
- No overage without your written approval; hours reported weekly in your own tool
- Effort basis: phase 1 ≈ 75 person-days; phases 2-3 sized from measured velocity at the gate

Phase	Price	Payment
1 Velocity pilot (fixed)	€38,000	On gate acceptance
2 Core migration (capped)	€86,000	Monthly, on velocity report
3 Cut-over + handover (fixed)	€44,000	On business sign-off
Total	**€168,000** (VAT 0%)	30 days net
