Varma Mutual Pension Insurance Company

Three models in production on one reusable MLOps pattern, built with your new specialists

Recordly proposal | Lab-to-production MLOps | 29 October 2026

Three prioritised use cases in production in 6 months on one reusable pattern, €95,200 fixed

- **One MLOps golden path** on your existing cloud data platform replaces isolated deployment scripts and per-model configurations
- **Quick win:** use case 1 in production with monitoring by the end of month 2
- **Your new specialists own it:** they co-build use case 2 and build use case 3 themselves, with us reviewing
- **Team of 3, majority planned at signing, confirmed in writing;** your right to require replacement accepted
- **€95,200 fixed**, paid at three accepted milestones; your procurement terms accepted without deviations
- Leadership quick win: lead time from approved model to production, measured from use case 1 and reported monthly

One MLOps golden path for every model, instead of one-off deployment work per experiment

- Every model, current and future, uses the same repo template, configuration schema, pipeline and monitoring. A new use case starts from the template, not from a blank script.
- Built on your existing cloud data platform; MLflow-compatible registry, so the pattern is not tied to one vendor.

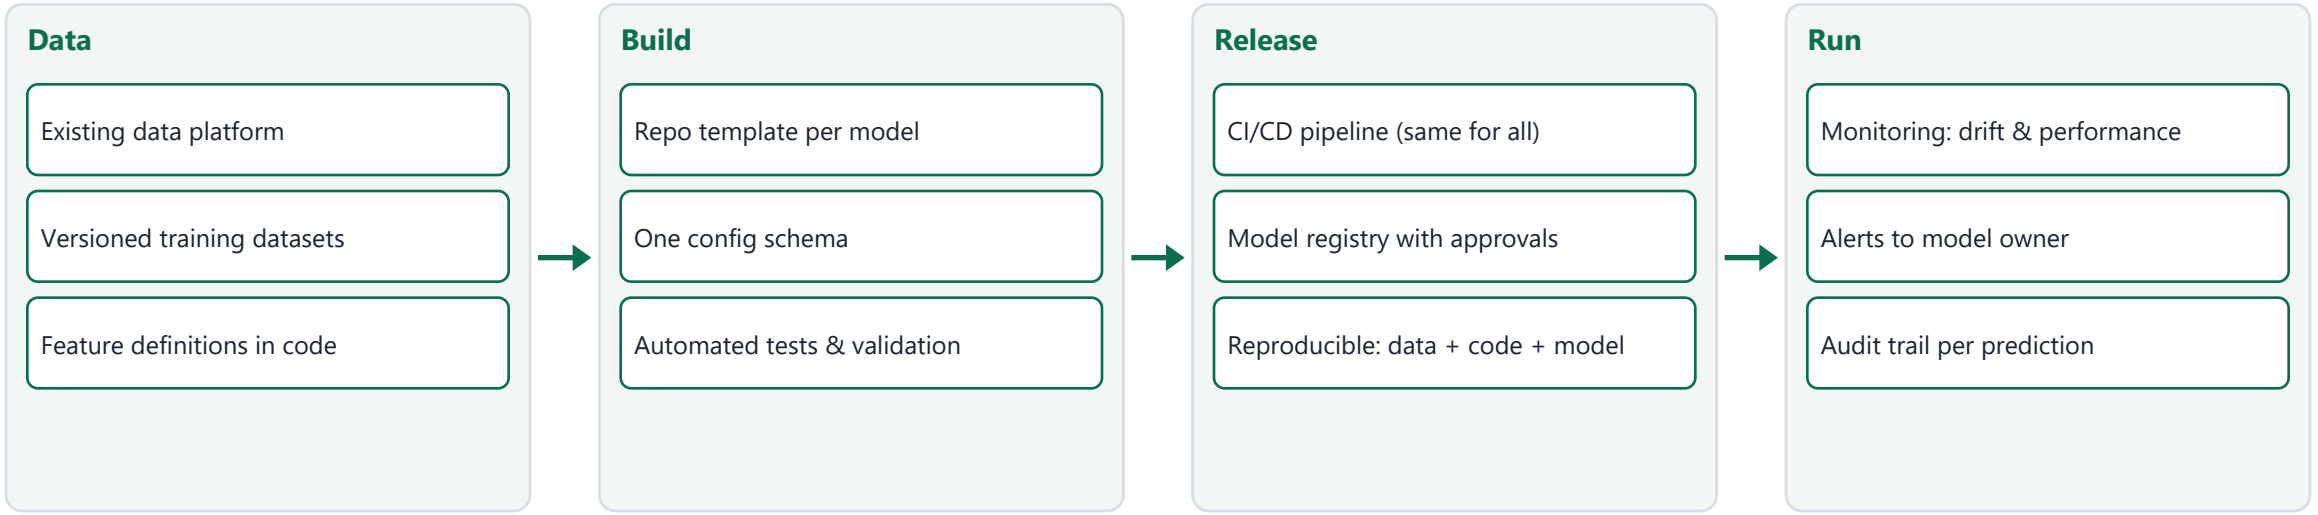

Models support pension decisions, they do not make them: human approval stays in the process, and explanations are logged

Use case 1 in production by month 2; your new specialists ship use case 3 themselves

Month	Use case	Who builds	Technical proof
1–2	Use case 1 on the golden path (quick win)	Recordly, your specialists pairing	In production with monitoring
3–4	Use case 2 on the same template	Your specialists, Recordly pairing	Built without new deployment scripts
5–6	Use case 3 + triage of the other ~17 experiments	Your specialists lead, Recordly reviews	Handover check: your team releases unaided

Technical unknowns we price in: which of the three use cases has production-ready data; access to personal data for training (minimised, pseudonymised); EU AI Act classification per use case. Documentation uses Finnish pension terms (työeläke, TyEL, eläkepäätös), no translation needed.

A proposed certified team, planned from signing, that leaves your team in charge

- **Replacement:** at your request, equal seniority within 10 working days, 2-week overlap at our cost
- **Delivery governance:** monthly steering with a written status (use cases, model health, risks); no weekly status meetings
- **Handover:** runbooks, the template and onboarding guide in Finnish, in your repos
- You may recruit our consultants after 12 months, with no fee

Name	Role	Allocation	Certifications	Available
Elina Mäkelä	Lead ML engineer	100%	Databricks Certified Machine Learning Professional; Microsoft Azure Data Scientist Associate	At signing
Jussi Heikkinen	MLOps / platform engineer	60%	Databricks Data Engineer Professional; Microsoft DevOps Engineer Expert	At signing
Tuomas Rantanen	Solution architect, delivery governance	15%	Microsoft Azure Solutions Architect Expert	At signing

€95,200 fixed across three accepted milestones, with the assumptions stated

Milestone	Content	Price	Payment
1 (month 2)	Golden path + use case 1 in production	€38,400	On acceptance
2 (month 4)	Use case 2 co-built with your specialists	€28,400	On acceptance
3 (month 6)	Use case 3 built by your team, triage of other experiments, handover	€28,400	On acceptance
Total		**€95,200** (VAT 0%)	30 days net

Assumptions: the three use cases are agreed in week 1; access to the cloud data platform and training data from week 1; no new licences (open MLflow-compatible registry on your platform). Risks: data readiness of a use case (swapped at milestone 1 if blocked) and EU AI Act classification (assessed in month 1). Your standard procurement terms accepted.
