RECORDLY

Analytics tickets in, reviewed pull requests out

An agent that drafts the code. Your people approve every change. Everything stays in Aktia's perimeter. €61,080 fixed total, Aktia's standard terms.

Proposal to Camilla Engblom, Head of Data and Analytics · Recordly Oy · Helsinki

Supplier profile, financial standing, subcontractors

Supplier	Recordly Oy, Helsinki. Data and AI consultancy. Our own agent product, the Virtual Data Engineer, is the pattern we propose here
Financial standing	Latest financial statements and a third-party credit report supplied with the formal tender
Subcontractors	**None.** Recordly employees only. Any later change needs Aktia's written approval


Concrete AI implementation case examples

CASE (RECORDLY AGENT TEAM ON SNOWFLAKE + DBT)	MEASURED RESULT
Semi-complex pipeline: build, test, validate. A person approves the PR	**12 h by hand → 30 min**
Migration Matillion + Redshift → dbt + Snowflake, jobs included (a migration cost, not a cost per ticket)	**~30 Snowflake credits** per migrated table
Pipeline and availability questions answered in the chat thread	Developer context switches per day: **several → 0**

> These are our results, not Aktia's. Your own baseline (ticket lead time, review load) is measured in Definition, so the pilot is judged on your numbers.

Technical solution architecture

The agent drafts, a person merges. One loop inside Aktia's tenant, with no path around review.

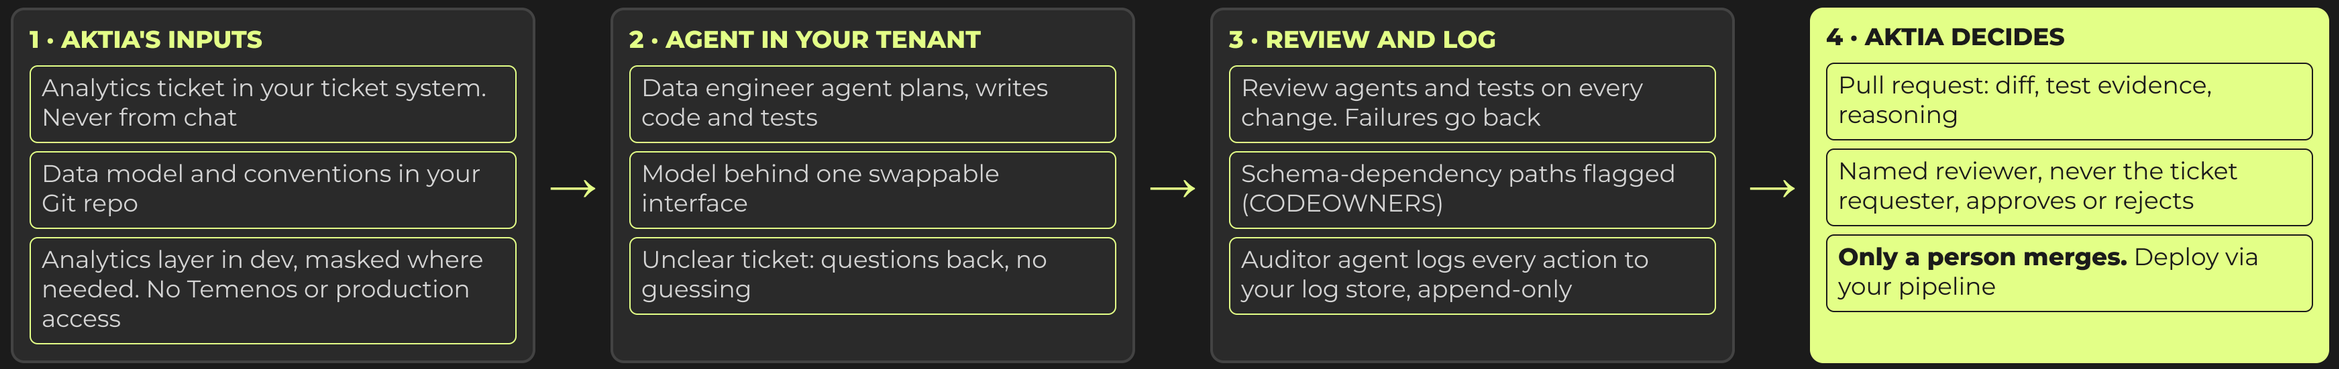

- **Your stack, honestly:** the RFP says "current data setup" and "public cloud"; ticket system and Git host are assumed. **Week 1 confirms all three.** On Snowflake + dbt we deploy our agent team. On another stack the agent is a new build, and scope is re-agreed at the gate. You can stop there.
- **Out of scope:** ML models or anomaly detection, new BI tools, extra use cases, any change to Temenos Transact. Only ticket → code → tests → pull request.

Compliance posture: FIN-FSA, EBA, DORA

WHAT YOU TOLD US	WHAT WE BUILD IN
Last winter a script bypassed peer review and altered schema dependencies	The agent **cannot approve or merge its own work.** Branch protection needs a named Aktia reviewer who is not the requester. Schema-dependency changes are blocked until the data owner approves. Week 1 bypass test: pushing or merging as the agent must fail
Supervisors scrutinise foreign-headquartered AI API dependencies	EU residency alone does not remove a foreign-HQ provider. Definition compares three hosting options with what each leaves: open-weight model in your tenant (no outside call); EU-headquartered provider; hyperscaler or Snowflake-hosted model in an EU region (foreign-HQ provider). **Aktia compliance chooses.** One swappable interface, exit tested
AI governance and operational resilience	Audit log in your log store, append-only, retention per your policy. A bad merge is reverted by a normal revert PR and logged in your DORA incident process. The agent stops when stuck. A control matrix maps each control to FIN-FSA, EBA and DORA requirements. Aktia compliance signs it off; we do not certify
Runbooks in English caused friction	Matrix, runbooks and training in **Finnish and Swedish**
IP	Everything made for Aktia (code, prompts, conventions, docs) is Aktia's property, stated in the contract

Technical gates and failure risks

Three gates before the agent touches real work

- **Week 1, integrations:** stack, ticket system, Git host and CI confirmed; bypass test passes
- **Week 3, Definition gate:** hosting options run on 20 of your tickets, reported with their exposure; Aktia picks one or stops. Baseline: rework rate, review minutes, lead time
- **Week 9, pilot gate:** approved-without-rework rate, review minutes and cost per ticket vs. baseline. Targets set at week 3; a miss means stop or adjust

FAILURE RISK	WHAT WE DO
Plausible but wrong PR; reviewer fatigue	Reasoning in every PR; review minutes and approval trend tracked; sampled second review
Prompt injection or vague ticket	Ticket is untrusted input; worst case is a PR a person rejects; unclear tickets go back
Flaky tests give a false green	Tests re-run; a pass a reviewer rejects is counted and reviewed
Model or provider changes behaviour	Pinned versions; your test set replayed before any switch; worse result blocks release
No model option good enough or accepted	Scope narrows to simple ticket types, or Aktia stops at the gate
Agent loops or gets stuck	Retry cap; it stops and writes what it tried

Core team: three seniors who do the work

	LEAD DATA ARCHITECT	SENIOR DATA ENGINEER	SENIOR AI ENGINEER
Required certifications	SnowPro Advanced: Architect · dbt Analytics Engineering	SnowPro Core · dbt Analytics Engineering	SnowPro Core · Microsoft Certified: Azure AI Engineer Associate
Required languages	Finnish required, Swedish, English	Finnish required, English	Finnish required, English
Availability	From signature, start date fixed in the contract	From signature	From signature

- **Swedish:** every Swedish deliverable is reviewed by a native Swedish speaker before delivery
- **Key-person terms:** named people, substitution only with Aktia's approval, equal seniority, overlap at our cost, financial penalty if breached. Aktia may require replacement at any time

Delivery plan and timeline

PHASE	WEEKS	WHAT HAPPENS	GATE
Definition	1–3	Confirm stack. Baseline on 20–30 recent tickets. Control matrix (FI/SV). Model-hosting options. Pick 2–3 ticket types	**Aktia decides go/no-go**
Delivery	4–9	Conventions and "perfect examples" written with your engineers. Agent team deployed in your tenant. Supervised pilot on the chosen ticket types	Merged-without-rework rate, test pass rate, review minutes per PR, run cost per ticket vs baseline. Targets set at week-3 gate; a miss means stop or adjust
Ongoing operations	10–22	Agent in run mode on a fixed 3-month term. **Aktia staff approve every change.** About 1 architect day per month from us	Scale, adjust or stop

- Your engineers co-build from week 1 and own conventions, prompts and code. Nothing is handed over at the end
- **No status meetings.** Written update every two weeks
- **Unknowns:** ticket quality (unclear tickets get questions back, not guesses; measured on the baseline set) and stack fit (week 1)

Preliminary pricing: definition, delivery, ongoing operations

Fixed total: €61,080 (excl. VAT)

PHASE	DAYS × DAY RATE	AMOUNT
Definition	AI architect 5 d × €960 + AI engineer 3 d × €960	€7,680
Delivery	AI architect 8 d × €960 + Data engineer 12 d × €920 + AI engineer 5 d × €960	€23,520
Ongoing operations	Agent team 3 months × €9,000 + AI architect 3 d × €960	€29,880

- **36 human days at €920–960/day**, plus the agent team on a **fixed 3-month term from go-live**. Pilot runs in Delivery are included
- **Stop after Definition** and pay only that phase. Invoiced per phase on acceptance, 21 days net
- **Licences:** none from Recordly. Model compute is billed to Aktia under the hosting option Aktia compliance chooses (on Snowflake, as AI credits on your account)
- **No contractual deviations.** Aktia's standard terms and key-person penalties accepted

Staffing review / Rauno: role profiles are requirements, not verified people. Confirm CVs, certificates, languages and actual availability before submission. One day = 8 hours; DE minimum EUR 115/h, DA EUR 125/h, AI expertise adds EUR 5/h for the relevant specialist. Architect base EUR 115/h is proposed for owner confirmation, not a user-supplied minimum. At most two architects. Validate fixed scope and risk allowance before commitment.

Architect effort: definition 5 days + setup 8 + run review 3 = 16 days, including the AI premium. DE 12 + AI engineer 8 = 36 human days total. Customer approves run changes.
