RECORDLY

Data platform architecture and tool selection, starting with a short scoping sprint

Built on BigQuery, Cloud Composer, Looker and Power BI. A gate before any milestone is locked. €20,240 fixed. Recruiting after 12 months accepted, no fee.

Proposal to Kirsi Suominen, Director of Enterprise Data Platforms · Recordly Oy · Helsinki


What we read between the lines

Each past problem in your brief becomes a safeguard

WHAT YOU TOLD US	OUR SAFEGUARD
Earlier advisory initiative **stalled: milestones locked before a scoping exercise**	**Paid scoping sprint first (4 days).** Milestones and scope are fixed only at **Gate 1**, after your steering committee has seen the sprint result.
Consultants' **billable hours stayed static** while automation sped them up	**Fixed price per deliverable**, no timesheets. If a deliverable is accepted in fewer days than planned, half of the unused days are credited.
Engineers' calendars eaten by **endless working sessions**	**Max 3 sessions of 60 min** in total, for named platform leads only. Everything else async: written questions and updates in your chat tool.
Steering committees and strict procurement	A one-page decision summary at each gate. Your standard procurement terms, **no deviations**.
Recruit consultants **after 12 months without a fee**	**Accepted as written.**

Solution approach: real-time where it pays, honest where it does not

Your brief requires real-time access to all data with no batch. Our honest answer: **real-time where a domain needs it**; literal zero-batch is not achievable for reconciled finance. Freshness per domain, agreed at Gate 1.

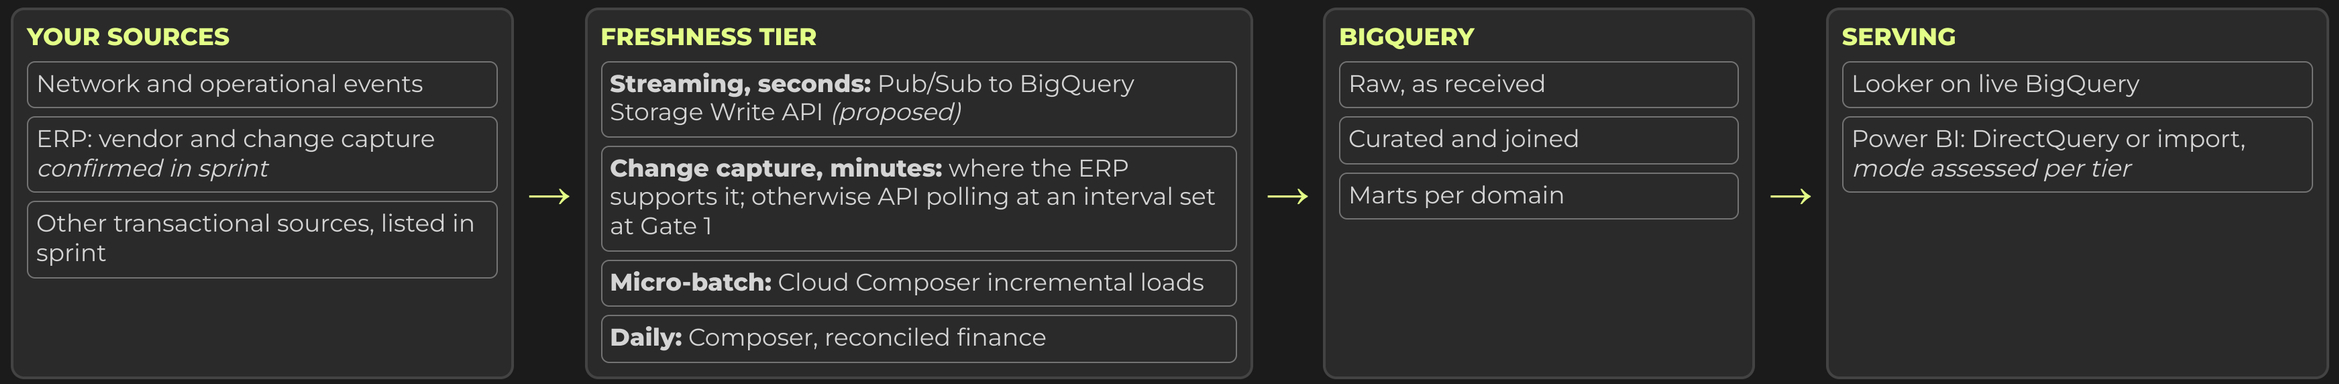

- **Each domain gets the slowest tier that still meets its tested need.** Target ranges per tier are agreed at Gate 1, after current freshness is measured.
- **Why not everything real-time:** finance close reconciles daily; streaming all data raises run cost, failure surface and retention exposure of traffic data. "All real-time" is scored with its cost; your committee decides.
- **Out of scope:** no AI or ML, no new licence or platform unless an existing service fails a tested need.

Technical gates: nothing is locked before it is measured

GATE	WHEN	PASSES WHEN
Access ready	Before sprint day 1	NDA and secrecy undertaking signed; read-only Elisa-issued roles on BigQuery, Composer and Looker metadata and logs. No subscriber rows leave your GCP project; plus a write-enabled sandbox dataset and one feed, in your project, for the latency test (synthetic or masked data only)
Gate 1	End wk 2	Each priority domain (3–5) has an owner, a stated freshness need and current freshness measured from Composer and BigQuery logs; one real feed run Pub/Sub to BigQuery to Looker in the sandbox dataset, end-to-end latency measured; ERP named with its change-capture options; target range per tier agreed
Checkpoint B	Wk 8	Options A current stack tuned, B tiered, C all real-time scored on latency, cost and quota per tier, failure mode and effort; one tier test on one domain, end-to-end latency measured against the Gate 1 range
Final	Wk 10	Target architecture and roadmap accepted by the steering committee; anything untested marked "not tested"

HONEST UNKNOWN	HOW IT IS SETTLED
ERP and its change capture	Sprint. Without change capture the ERP domain runs API polling or micro-batch, and Gate 1 shows its measured delay against the stated need
Sandbox dataset and feed	Requested before day 1. If none by day 3, the latency test is marked "not tested" and streaming stays a proposal
Power BI connectivity	Import refreshes on a schedule; DirectQuery freshness is bounded by query load, limits and cost. Measured per report in the sprint
Where Composer code, CI/CD and access policies live	Recorded in the sprint. Existing pipelines stay unless a test fails

Implementation plan: sprint, gate, then assessment

PHASE	WEEKS	PERSON-DAYS	OUTPUT
0 · Scoping sprint	1–2	4	Current-state sketch, freshness need and measured current freshness per domain, ERP change-capture check, **proposed milestones**
Gate 1	end wk 2	–	Steering committee decides: **go, adjust or stop**. If stop, you pay for the sprint only.
A · Current state and requirements	3–5	6	Architecture baseline, requirements by domain, tiered freshness map
B · Options and tool selection	5–8	7	Options scored on cost per tier, risk, latency and effort; one tier test on one domain; recommendation
C · Target architecture and roadmap	8–10	5	Target architecture with a freshness tier per domain, sequenced roadmap, risks, one-page steering summary

- Deliverables fixed per phase after Gate 1; documents in Finnish or English, as you prefer.
- **Your time:** about 3 hours per engineer in total.

Team capabilities and availability

	LEAD DATA ARCHITECT	SENIOR DATA ENGINEER
Required certifications	Google Cloud Professional Cloud Architect · Google Cloud Professional Data Engineer	Google Cloud Professional Data Engineer · Microsoft Certified: Power BI Data Analyst Associate
Required languages	Finnish required, English	Finnish required, English
Days	13	9
Availability	**Target at signature; evidence pending**	**Target at signature; evidence pending**

Two senior people who do the work themselves. No subcontractors. Replacement of any consultant at your request, equal seniority, overlap at our cost.

Pricing and terms

Fixed total: €20,240 (excl. VAT)

ROLE	PERSON-DAYS	DAY RATE (8 H)
Lead Data Architect	13	€920
Senior Data Engineer	9	€920
Total	**22 days**	**22 × €920 = €20,240**

- **Fixed price per deliverable**, invoiced on acceptance (sprint, A, B, C); 21 days net
- **Gate 1 exit:** stop after the sprint and you pay for its 4 days only (4 × €920)
- **Licences:** none; your existing Google Cloud, Looker and Power BI
- Effort above plan is Recordly's risk. Travel in Helsinki included.

CONTRACT TERMS

No contractual deviations. Elisa may recruit deployed consultants after 12 months **without a fee**.

Staffing review / Rauno: role profiles are requirements, not verified people. Confirm CVs, certificates, languages and actual availability before submission. One day = 8 hours; DE minimum EUR 115/h, DA EUR 125/h, AI expertise adds EUR 5/h for the relevant specialist. Architect base EUR 115/h is proposed for owner confirmation, not a user-supplied minimum. At most two architects. Validate fixed scope and risk allowance before commitment.
