RECORDLY

Data platform architecture and tool selection, starting with a short scoping sprint

Built on BigQuery, Cloud Composer, Looker and Power BI. A gate before any milestone is locked. €20,240 fixed. Recruiting after 12 months accepted, no fee.

Proposal to Kirsi Suominen, Director of Enterprise Data Platforms · Recordly Oy · Helsinki


What we read between the lines

Each past problem in your brief becomes a safeguard

WHAT YOU TOLD US	OUR SAFEGUARD
Earlier advisory initiative **stalled: milestones locked before a scoping exercise**	**Paid scoping sprint first (4 days).** Milestones and scope are fixed only at **Gate 1**, after your steering committee has seen the sprint result.
Consultants' **billable hours stayed static** while automation sped them up	**Fixed price per deliverable**, no timesheets. If a deliverable is accepted in fewer days than planned, half of the unused days are credited.
Engineers' calendars eaten by **endless working sessions**	**Max 3 sessions of 60 min** in total, for named platform leads only. Everything else async: written questions and updates in your chat tool.
Steering committees and strict procurement	A one-page decision summary at each gate. Your standard procurement terms, **no deviations**.
Recruit consultants **after 12 months without a fee**	**Accepted as written.**

Solution approach: real-time where it pays, honest where it does not

Your brief requires real-time access to all data with no batch. Our honest answer: **real-time where a domain needs it**; literal zero-batch is not achievable for reconciled finance. Freshness per domain, agreed at Gate 1.

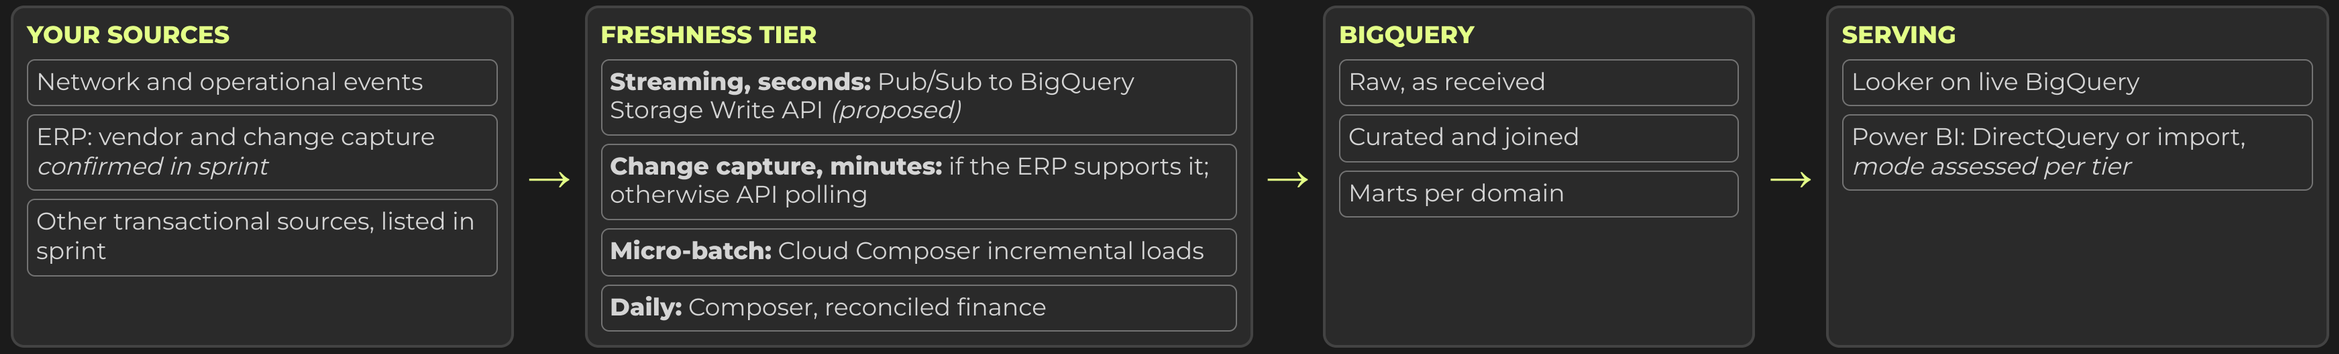

- **Each domain gets the slowest tier that still meets its tested need.** Target ranges per tier are agreed at Gate 1, after current freshness is measured.
- **Why not everything real-time:** finance close reconciles daily; streaming all data raises run cost, failure surface and retention exposure of traffic data. "All real-time" is scored with its cost; your committee decides.
- **Out of scope:** no AI or ML, no new licence or platform unless an existing service fails a tested need.

Technical gates: nothing is locked before it is measured

GATE	WHEN	PASSES WHEN
Access ready	Before sprint day 1	NDA and secrecy undertaking signed; read-only Elisa-issued roles on BigQuery, Composer and Looker metadata and logs, plus a sandbox dataset for the latency test. No subscriber rows leave your GCP project
Gate 1	End wk 2	Each priority domain (3–5) has an owner, a stated freshness need and current freshness measured from logs; one real feed run Pub/Sub → BigQuery → Looker, end-to-end latency measured; ERP named with its change-capture options; target range per tier agreed
Checkpoint B	Wk 8	Options A current stack tuned, B tiered, C all real-time scored on latency, cost and quota per tier, Composer load, failure mode and effort; every score cites a measurement or is marked "not tested"
Final	Wk 10	Target architecture and roadmap accepted by the steering committee; anything untested marked "not tested"

HONEST UNKNOWN	HOW IT IS SETTLED
Which ERP and its change capture	Sprint. Without CDC, API polling or micro-batch at an interval set at Gate 1, shown to the steering committee
Power BI connectivity	Import refreshes on a schedule; DirectQuery freshness is bounded by query load, limits and cost. Measured per report in the sprint
Where Composer code, CI/CD and access policies live	Recorded in the sprint. Existing pipelines stay unless a test fails

Implementation plan: sprint, gate, then assessment

PHASE	WEEKS	PERSON-DAYS	OUTPUT
0 · Scoping sprint	1–2	4	Current-state sketch, freshness need and measured current freshness per domain, **measured latency test** (Pub/Sub → BigQuery → Looker, one real feed), ERP change-capture check, **proposed milestones**
Gate 1	end wk 2	–	Steering committee decides: **go, adjust or stop**. If stop, you pay for the sprint only.
A · Current state and requirements	3–5	6	Architecture baseline, requirements by domain, tiered freshness map
B · Options and tool selection	5–8	7	Options scored on cost (streaming, live-query, quotas, Composer load), risk, latency and effort; recommendation
C · Target architecture and roadmap	8–10	5	Target architecture with a freshness tier per domain, sequenced roadmap, risks, one-page steering summary

- Deliverables fixed per phase after Gate 1; documents in Finnish or English, as you prefer.
- **Your time:** about 3 hours per engineer in total.

Team capabilities and availability

	LEAD DATA ARCHITECT	SENIOR DATA ENGINEER
Required certifications	Google Cloud Professional Cloud Architect · Google Cloud Professional Data Engineer	Google Cloud Professional Data Engineer · Microsoft Certified: Power BI Data Analyst Associate
Required languages	Finnish required, English	Finnish required, English
Days	13	9
Availability	**Target at signature; evidence pending**	**Target at signature; evidence pending**

Two senior people who do the work themselves. No subcontractors. Replacement of any consultant at your request, equal seniority, overlap at our cost.

Pricing and terms

Fixed total: €20,240 (excl. VAT)

ROLE	PERSON-DAYS	DAY RATE (8 H)
Lead Data Architect	13	€920
Senior Data Engineer	9	€920
Total	**22 days**	**22 × €920 = €20,240**

- **Fixed price per deliverable**, invoiced on acceptance (sprint, A, B, C); 21 days net
- **Gate 1 exit:** stop after the sprint and you pay for its 4 days only (4 × €920)
- **Licences:** none; your existing Google Cloud, Looker and Power BI
- Effort above plan is Recordly's risk. Travel in Helsinki included.

CONTRACT TERMS

No contractual deviations. Elisa may recruit deployed consultants after 12 months **without a fee**.

Staffing review / Rauno: role profiles are requirements, not verified people. Confirm CVs, certificates, languages and actual availability before submission. One day = 8 hours; DE minimum EUR 115/h, DA EUR 125/h, AI expertise adds EUR 5/h for the relevant specialist. Architect base EUR 115/h is proposed for owner confirmation, not a user-supplied minimum. At most two architects. Validate fixed scope and risk allowance before commitment.
