Veikkaus Oy

Tech & architecture slides for the Veikkaus deck

Two slides for deck-writer: slide 1 is the 'Technical methodology and deliverables' section, slide 2 merges into 'Implementation plan and timeline'

We read evidence at every layer of your stack, labelled the way your brief labels it

- **Licence baseline first:** entitlement vs. actual use per multi-year commitment, from the admin and usage logs you have. A new component is proposed only where existing capacity fails a tested need.
- **Proof, not promises:** every finding is a card with log evidence and a compliance note, or is marked "confidence low, evidence requested". Options are scored on five weighted criteria from your brief; compliance is also a pass/fail gate.
- **Model deployment is measured, not rebuilt:** lead time and manual hand-offs per step on your in-house AI platform. Vendor-neutral: products are confirmed in week 1.

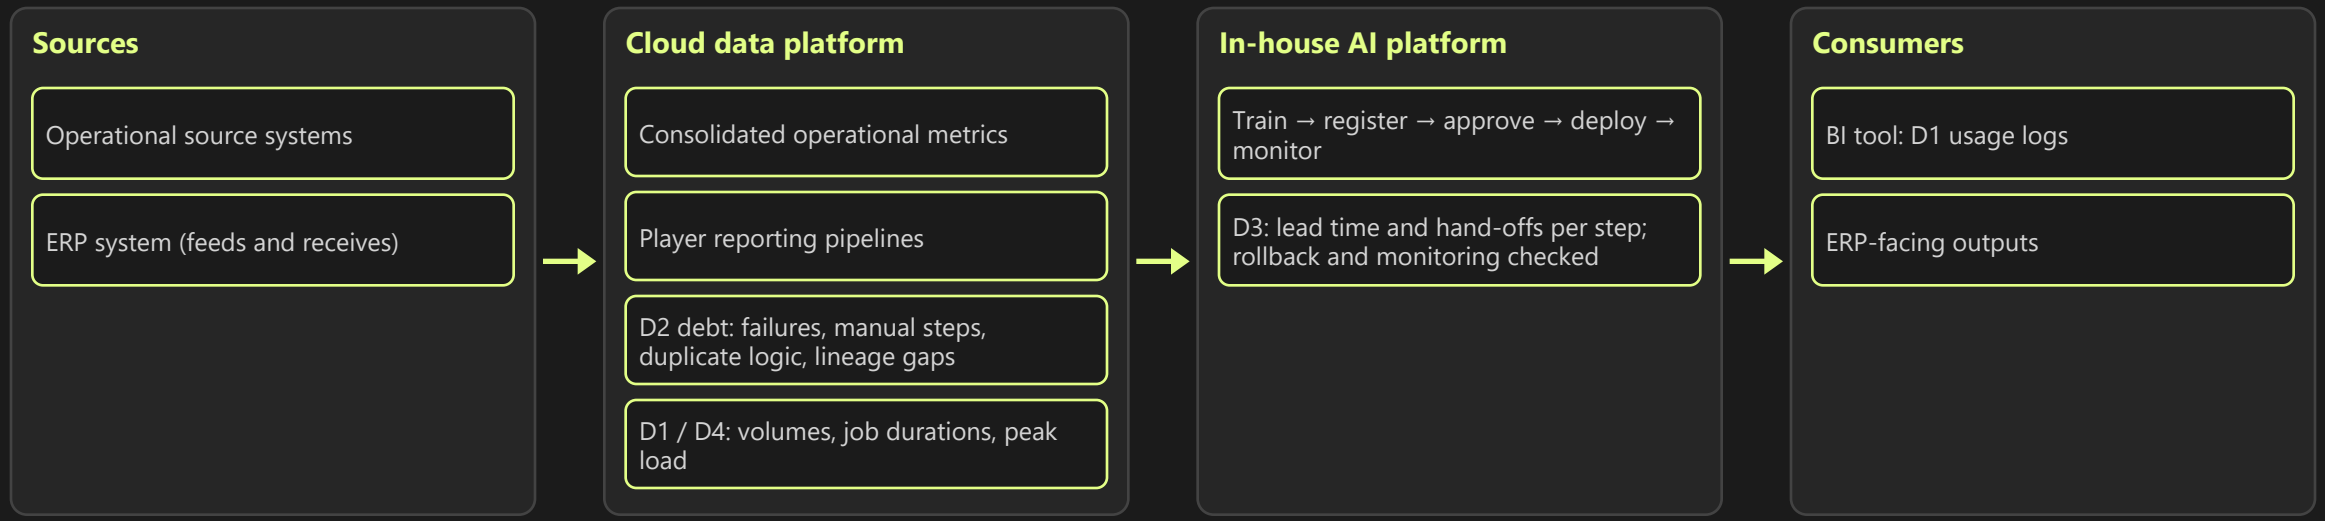

Scope map in your brief's own labels, not your confirmed architecture. Every finding: access control, audit trail, lineage, player-data handling.

Three gates keep the assessment honest: access, evidence quality, compliance

Gate	When	Pass criterion
Access and data handling	Week 1	Named read-only accounts issued by Veikkaus, access list and NDA signed; metadata and counts only. If approval is late, your admins export the logs and the plan moves by the delay
Evidence quality	Week 4 checkpoint	Target: ≥80% of commitments have usage data and ≥10 debt items are log-evidenced, confirmed with you after week 1. Scoring anchors agreed. Otherwise re-scope before phase 3
Compliance	Option scoring, weeks 5–7	An option that fails on access control, audit trail, lineage or player-data handling is not recommended, whatever its score
Roadmap	Week 8	Changes are proposed, never applied; every cut-over step has an owner and your approval

Technical unknowns: the products and licence terms behind "cloud data platform" and "in-house AI platform" (week-1 checklist); whether usage logs can be exported (gaps shown on the D1 cards); deployment history shorter than 6 months (lead time shown as a range); current volumes (throughput scored against measured load, no real-time promise).
